


PROJECT Margrave and Henderson St.

Continued From Page

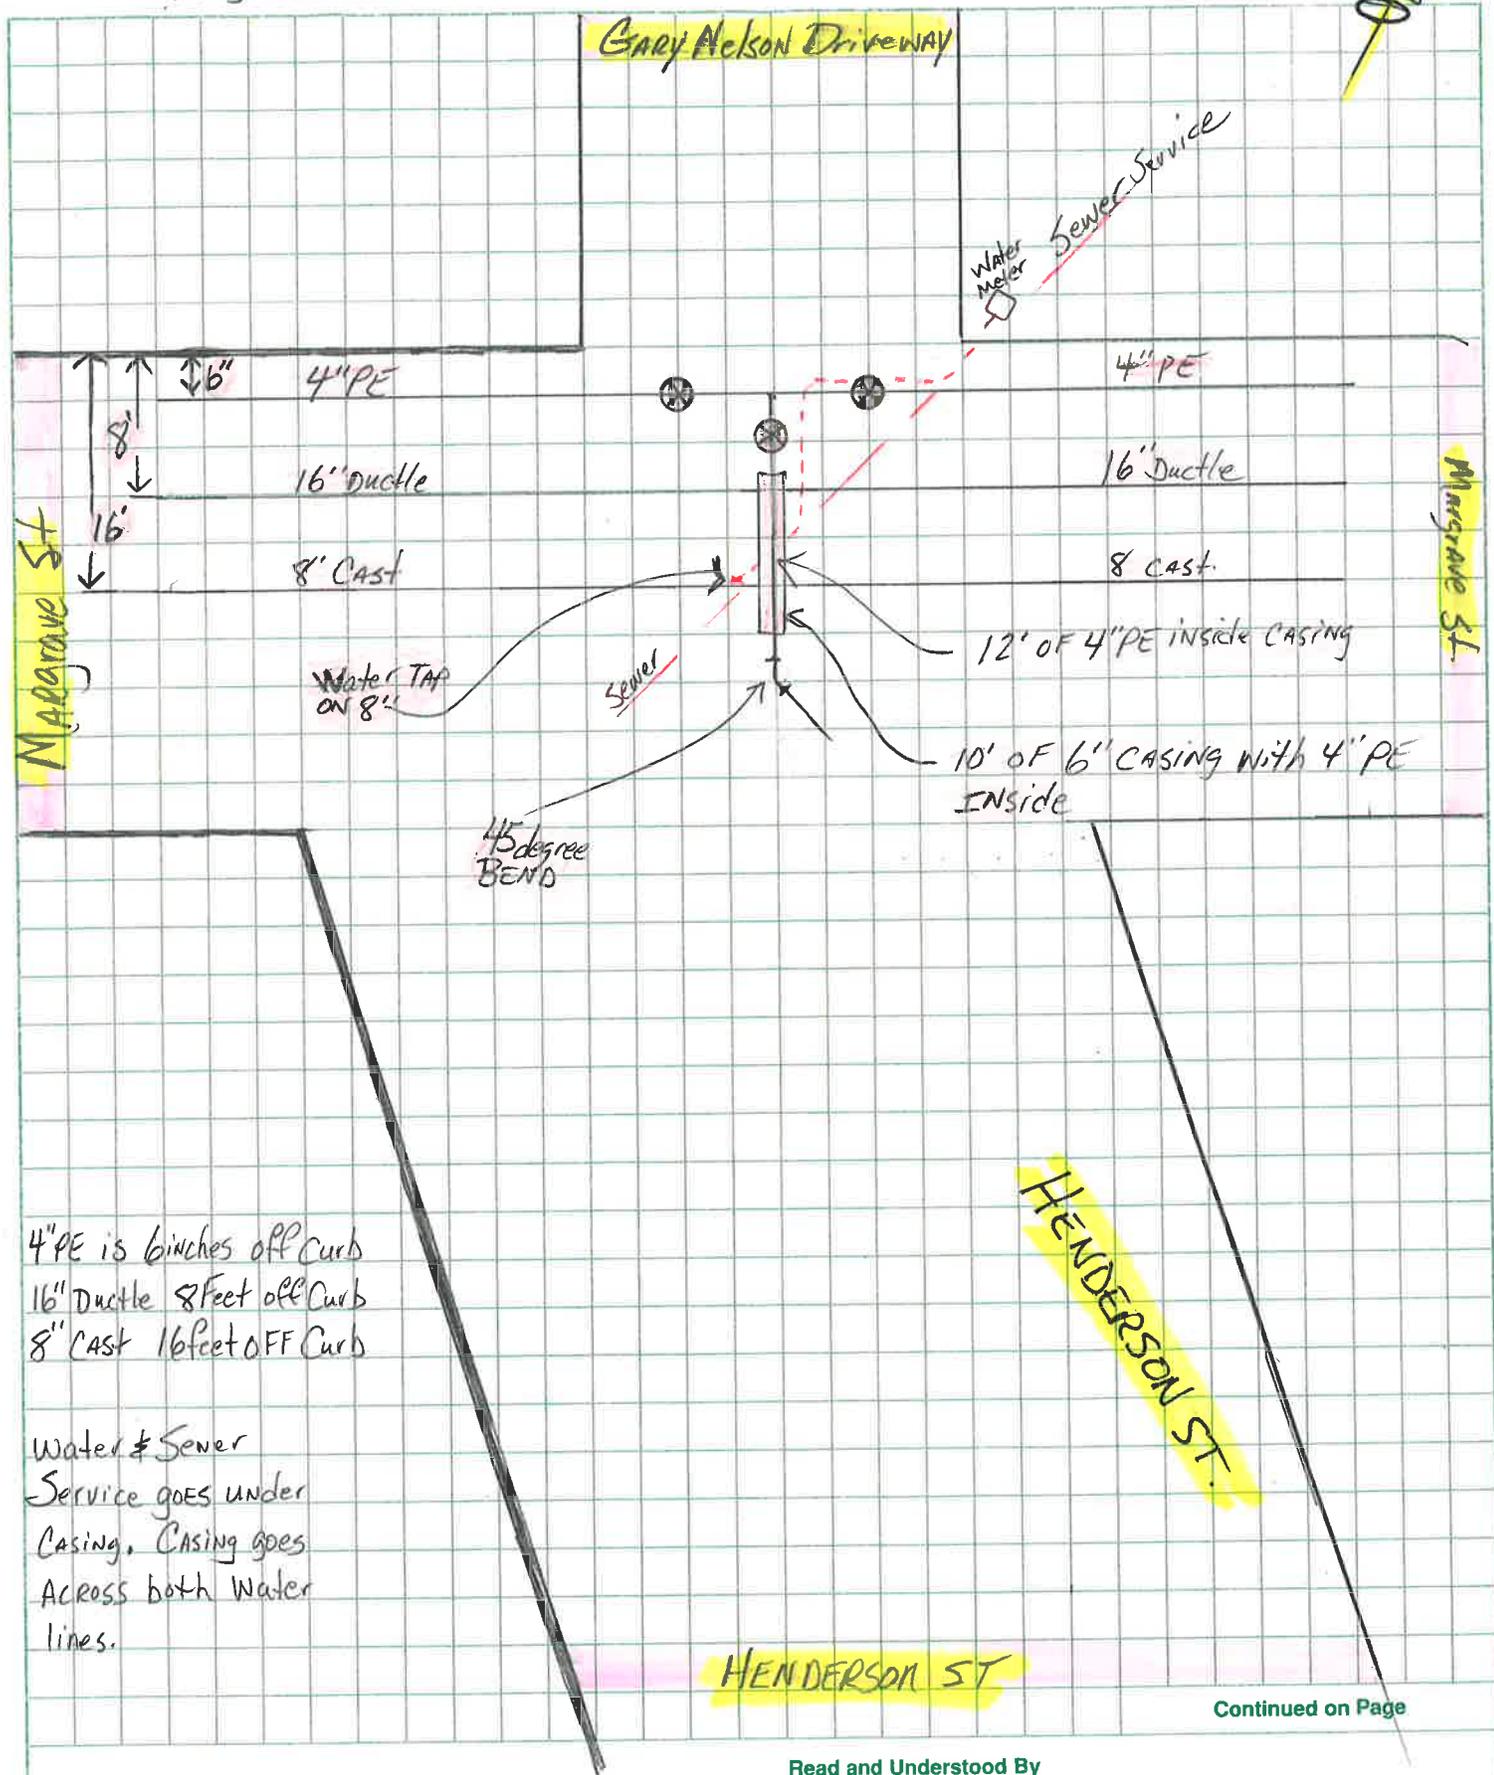

4" PE is 6 inches off Curb
 16" Ductile 8 Feet off Curb
 8" CAST 16 feet OFF Curb

Water & Sewer
 Service goes under
 casing, casing goes
 across both water
 lines.

HENDERSON ST.

HENDERSON ST

Continued on Page

Read and Understood By

Frankie Davis

3/26/20

Signed

Date

Signed

Date
